
SCRUM REPORT


Name: Nikita Mankani
SRN: PES1UG24CS300
Section: E
Problem Statement: #54 - Local Sports Tournament & Bracket Manager

1. Backlog with Epics and User Stories

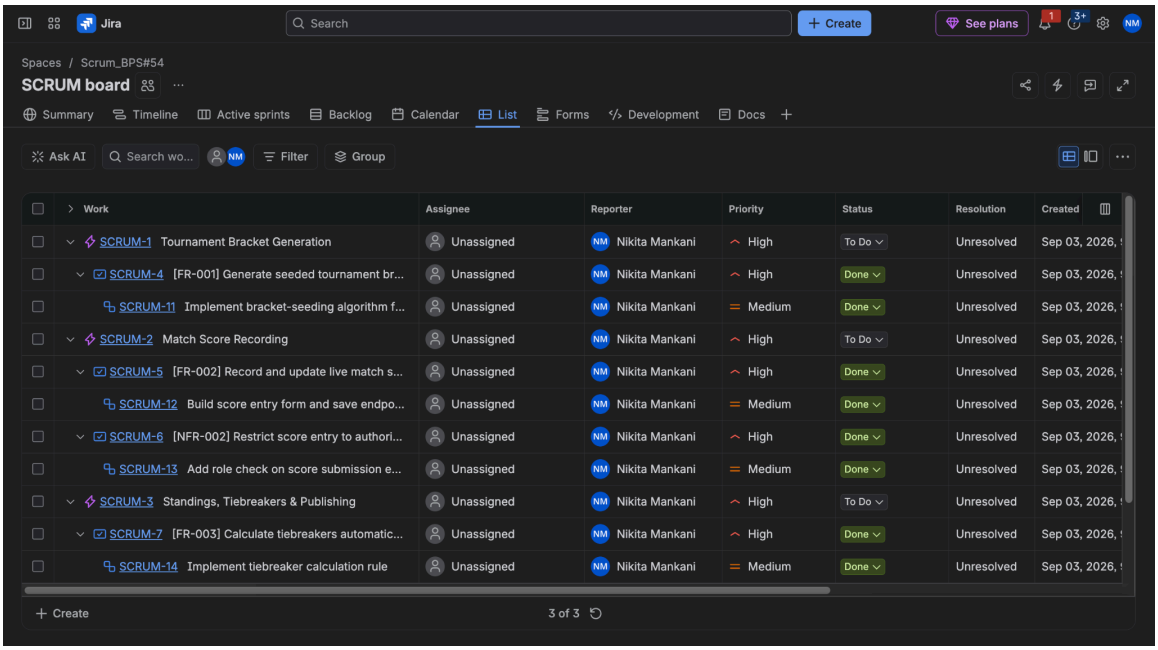


Same 3 epics and 7 stories as the Kanban project, since they both trace back to the same Lab 1 requirements table (FR-001 to FR-005, NFR-001, NFR-002). The difference here is that this project actually ran two sprints instead of just sitting on a board — Sprint 2 is active at the top, and the Backlog below it holds NFR-001 and FR-005, which haven't been finished yet.


2. Story Point Assignments

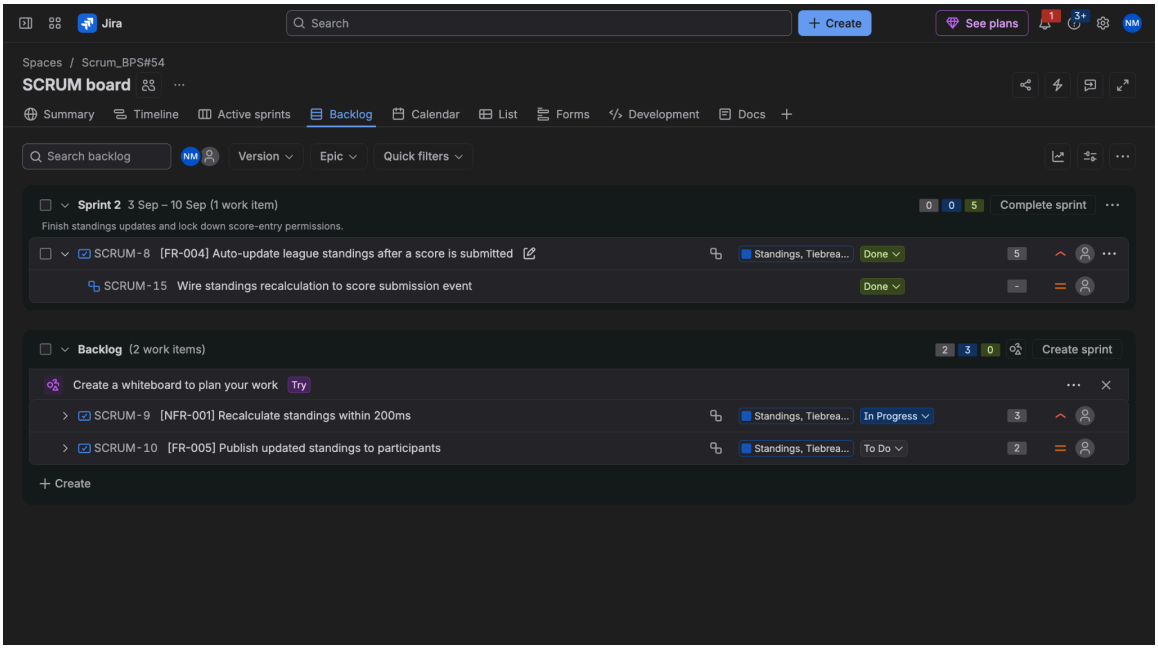

I estimated each story using the Fibonacci scale. Bracket generation got an 8 since it's the most algorithmically involved piece (seeding plus single/double elimination). Score recording and the standings-update story both got 5. The tiebreaker calculation also got 5. The two NFR stories (restricting score entry, and the 200ms performance target) got 3 each since they're more about constraints than new functionality. Publishing standings got the smallest estimate, 2, since it's mostly wiring an existing data set to a participant-facing view. Total backlog: 31 points across the two sprints and the leftover backlog.


3. Sprint Board - Active Sprint view

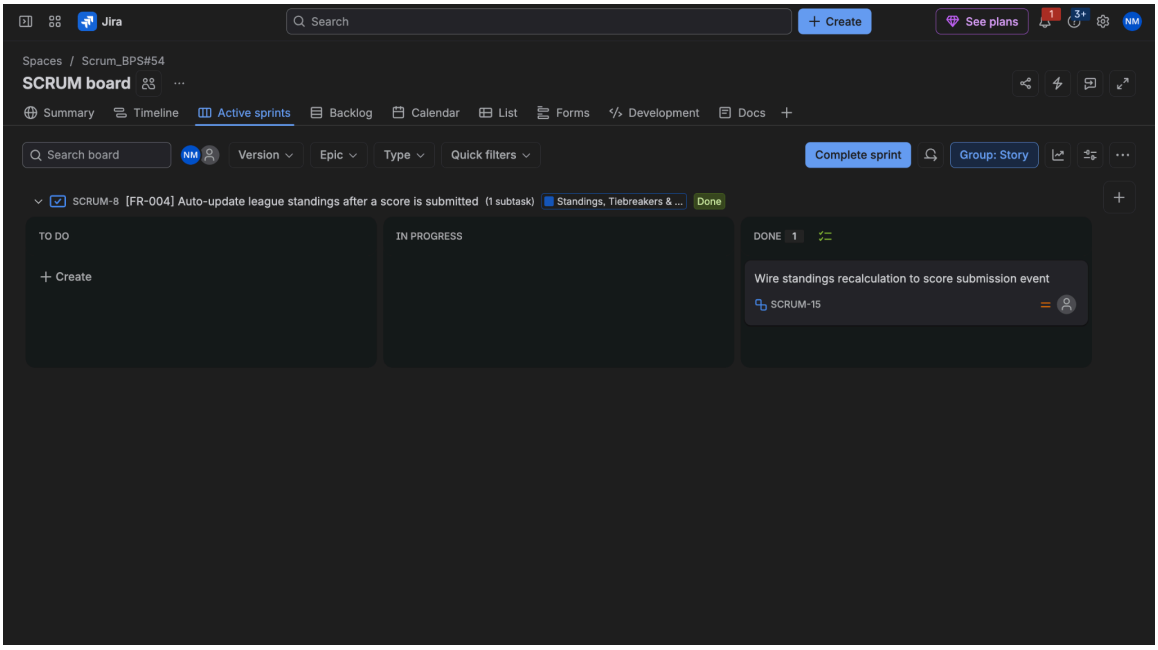

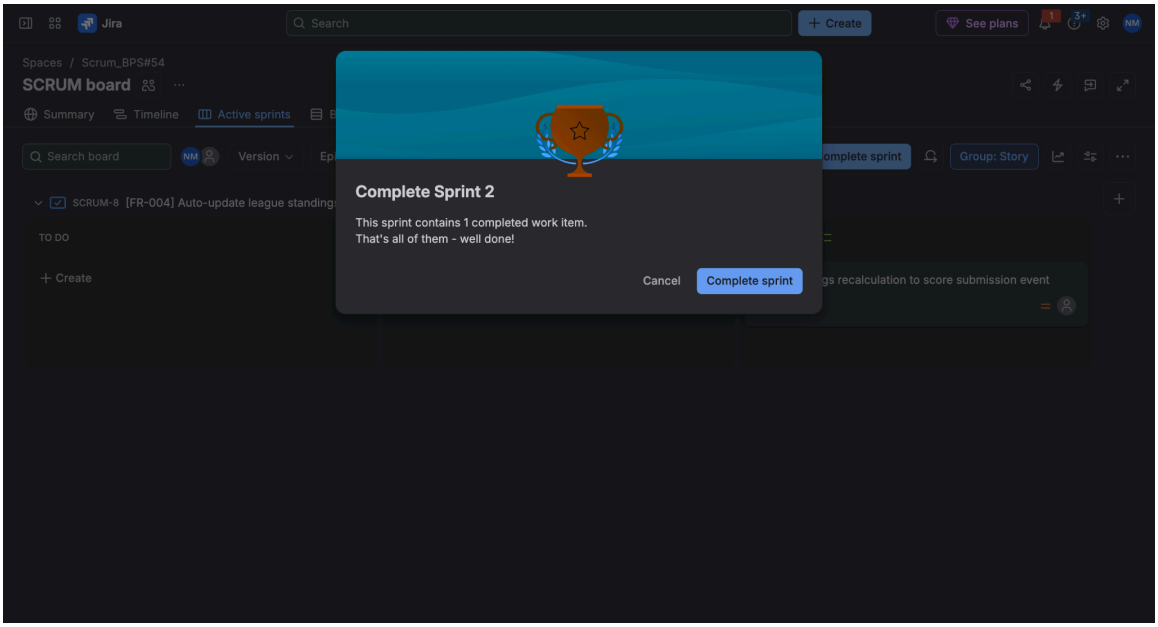

Sprint 1 ran with 4 stories (FR-001, FR-002, NFR-002, FR-003 - 21 points total) and all 4 got moved to Done, so Sprint 1 delivered its full commitment. Sprint 2 committed FR-004 and NFR-001 (8 points). FR-004 got finished and moved to Done, but partway through NFR-001 (the 200ms performance story) it became clear it wasn't going to get done in the time I had, so I pulled it back out of the sprint and into the backlog rather than leave it sitting there unfinished. FR-005 (publish standings) never got pulled into a sprint at all - it's still sitting in the plain backlog waiting for a future sprint. So the backlog isn't empty at the end of this: NFR-001 and FR-005 are both still there.

4. Sprint Report / Burndown

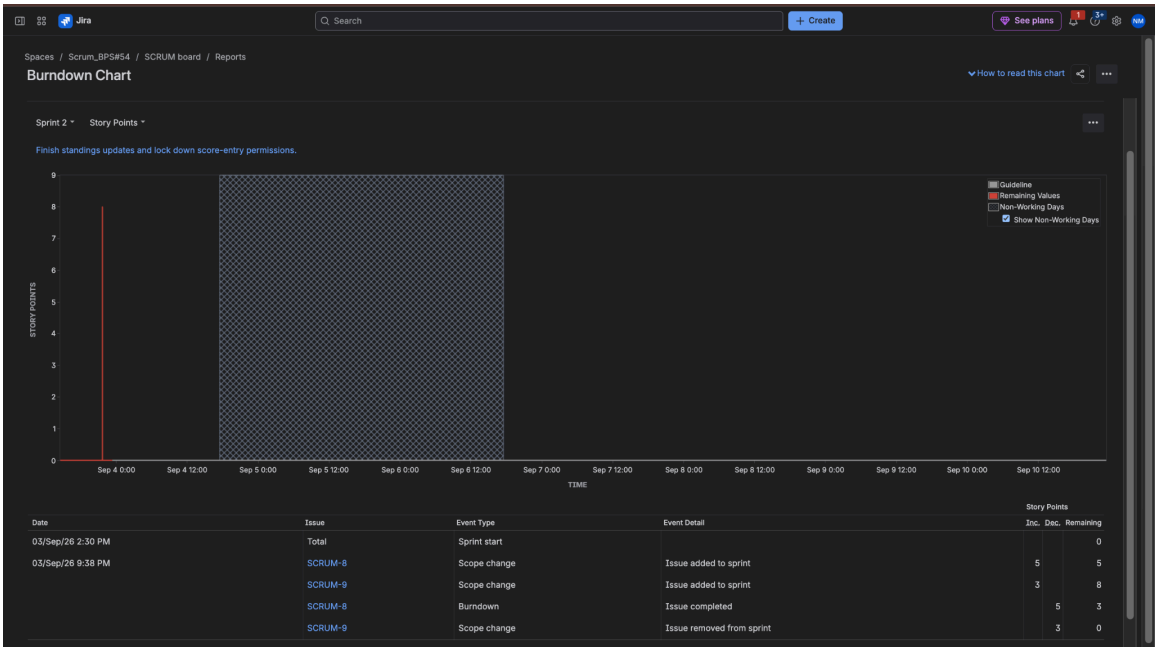

The chart and its event log below show exactly what happened in Sprint 2: both stories were added at sprint start (8 points total), FR-004 (SCRUM-8) was completed, and NFR-001 (SCRUM-9) was removed from the sprint once it was clear it wouldn't finish in time - that's the carry-over back to the backlog. One honest note: because I built and ran both sprints inside a single lab session instead of over two real weeks, the chart shows a steep, near-instant change rather than a smooth day-by-day decline - that's genuinely when the status changes happened, so I'm not pretending otherwise.

Reflection Questions

1. Did your estimations reflect the actual effort?

Mostly yes for Sprint 1 - all 4 stories I estimated got completed inside the sprint, so the 21 points felt like a fair commitment. Sprint 2 is where the estimate didn't hold up: I committed 8 points (FR-004 and NFR-001) but only delivered 5. NFR-001 was a 3-point estimate but the actual work of tying a 200ms performance target to a recalculation pipeline is the kind of thing that's hard to size accurately without doing some of it first - it's a performance/testing requirement, not a straightforward feature, so a flat story point number probably undersold how open-ended it is.

2. Was your backlog well-prioritized?

Broadly yes. I put the core functional path first - generating the bracket, recording scores, and the two directly related requirements - in Sprint 1, since none of the standings or publishing work makes sense without those existing first. FR-005 (publishing standings) was the one story I consistently pushed to the back because it's the lowest priority (Medium, vs High for everything else) and the smallest points, and that's exactly the story that's still sitting unstarted in the backlog, which I think is the right call under time pressure rather than a prioritization mistake.

3. How did your simulated sprint align with your plan?

Sprint 1 lined up with the plan exactly - everything committed got delivered. Sprint 2 didn't: I planned to close out both NFR-001 and FR-004, but only finished FR-004 in the time available and had to carry NFR-001 back to the backlog. That's a fairly normal Scrum outcome and not something I want to dress up - the plan was reasonable, the execution came up short on one item, and that's what carry-over is for.

4. What insights did the burndown chart give about your team's capacity?

Sprint 1's chart shows the full 21 points burning down to zero. Sprint 2's chart shows the line drop by 5 points when FR-004 was completed, then flatten out once NFR-001's 3 points were removed from the sprint instead of burning down. If I take these two sprints as a signal, my real sprint capacity looks closer to 21 points than 31 - Sprint 2 was over-committed relative to what actually got finished, which is useful to know for planning a Sprint 3.
